

Weekly Construction Status Update

Woodhaven Brownstown School District



Woodhaven High School

BP#3

3/11/19

Progress Overview

- Backfill pool 90% complete
- Gutter drain 80% complete
- All pool underground to be complete in two weeks.
- Pool overhead ongoing. (Ceiling clouds, paint, duct sock)

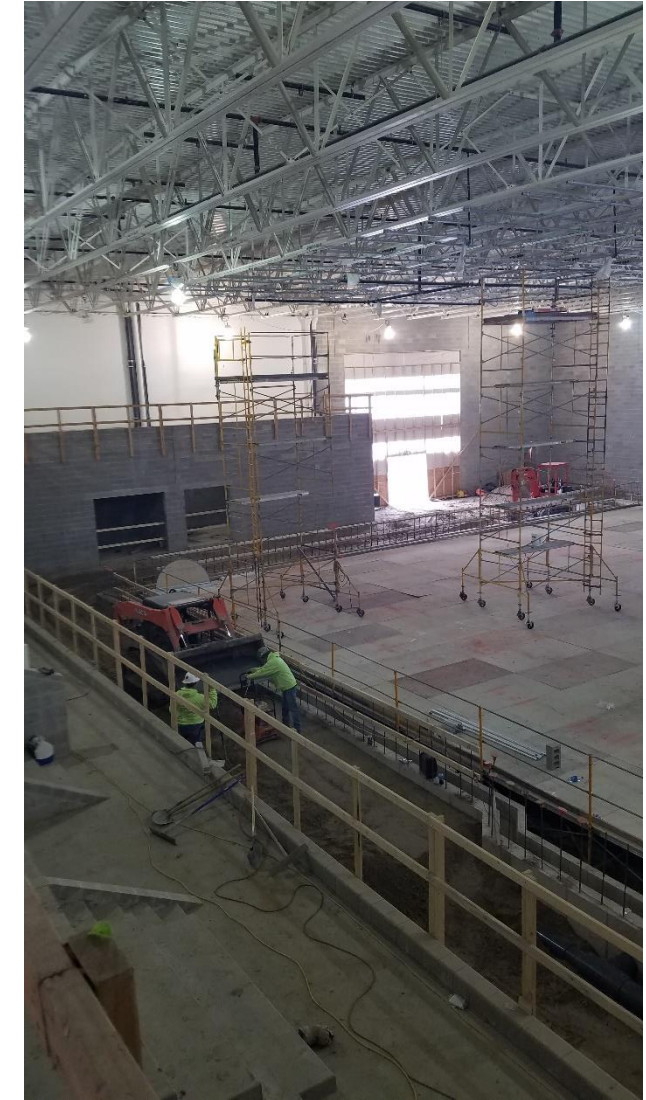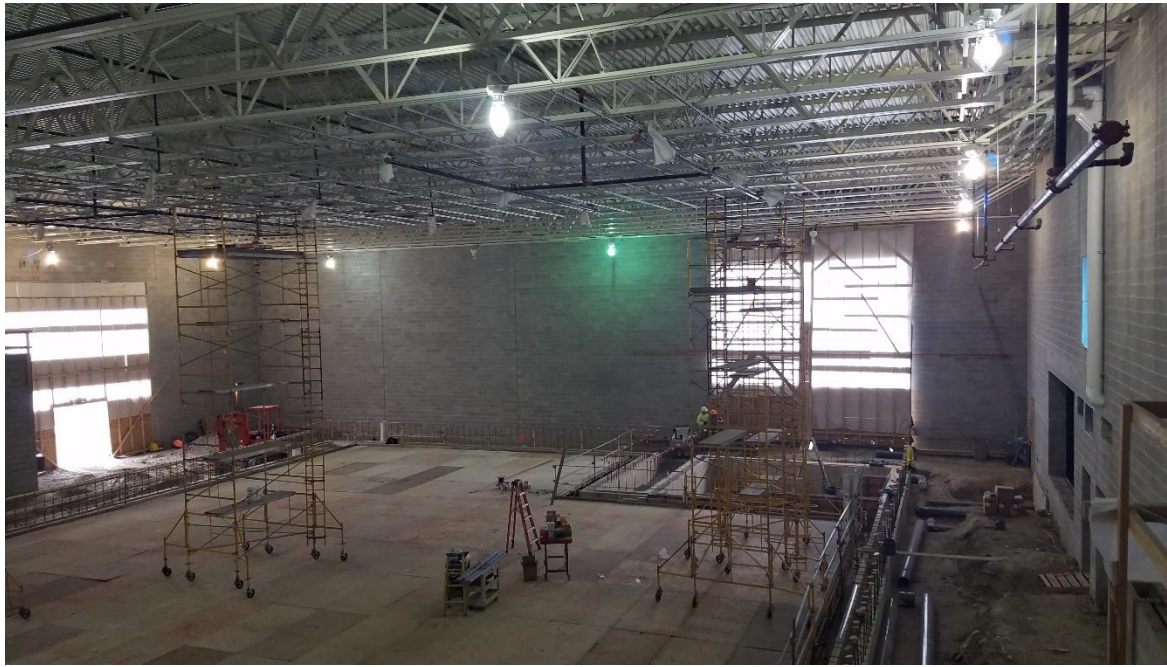

Progress Overview

- Gym electrical rough-ins ongoing.
- Start painting gym steel.



Progress Overview

- Brick wash complete and mechanical overhead complete.
- Gypsum bulkheads ongoing.
- Start grid soon in Athletic Lobby.



Two Week Look Ahead

- Install Gym overhead roughs and paint.
- Start tile in north locker room this week with the south locker room to follow.
- Install pool clouds and paint steel in Natatorium.
- Complete back fill and deck drain on pool deck.
- Pour pool deck.
